



Interreg
ITALIA-SLOVENIJA



GreenHull

GreenHull kick-off meeting

23.3.2020



ESOTECH



NACIONALNI INŠTITUT ZA BIOLOGIJO
NATIONAL INSTITUTE OF BIOLOGY



Agenda details



GreenHull

1. Introduction and overview of the project

Goals:

- ➔ Elect the: Team manager, Financial manager, Communication manager, and the Project board
- ➔ Define the: communication between partners, Managing authority and Public relations

2. Detailed project tasks, collaboration between partners and deliverables

Goals:

- ➔ Define clear tasks for each partner, workflow and deadlines
- ➔ Deliverables

3. Financial planning

Goals:

- ➔ Financial reporting & deadlines
- ➔ Equipment purchases & subcontracting

4. Various

- ➔ Media event organization in Venezia
- ➔ Next project meetings





Interreg
ITALIA-SLOVENIJA



GreenHull

1. Introduction and overview of the project





GreenHull project goals

Improve the environmental protection by:

- 1) Development of 2 innovative green technologies (IGT) for vessel in-water cleaning (ROV and a pilot modular wastewater treatment plant)

Problem:

- *reductions in vessel performance and fuel efficiency, and increases in emissions due to accumulation of aquatic organisms on immersed surfaces*
- *introduction and spread of marine non-indigenous species in local habitat*



- 2) Transborder cooperation and waste management due to vessel in-water cleaning procedure

Problem:

- *no common approach*

1. IGT

2. IGT

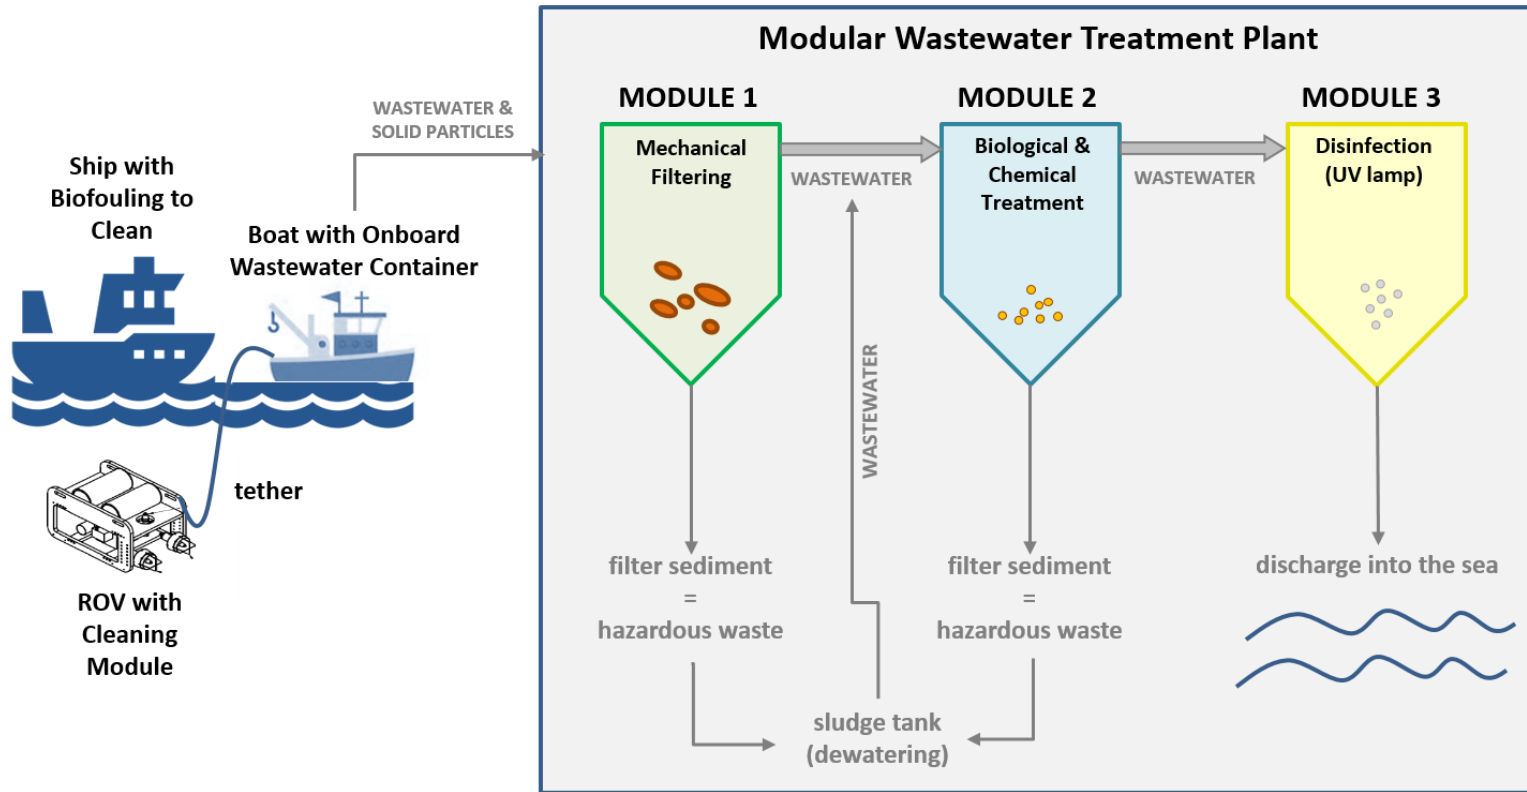



UNIONE
EUROPEA
EVROPSKA
UNIJA

Interreg
ITALIA-SLOVENIJA



GreenHull

Presentation



Project management

Project manager	→	Uros Puc (MPS)
Financial manager	→	Sergeja Vogrincic (MPS)
Communication manager	→	Caterina CD. Dabalà (CORILA)

Communication with the Managing Authority → LP is responsible for all PP
Public relations → CORILA

Project board:

- 1 person from each PP is reporting to LP and organizing internal communication
- Project board should take decisions about:
 - project execution and progress
 - deliverables and reports
 - solving project challenges and/or project/financial changes
 - project evaluation
 - etc.



Interreg
ITALIA-SLOVENIJA



GreenHull

2. Detailed project tasks, collaboration between partners and deliverables





GreenHull work packages (short description):

- WP0 → Project preparation (MPS)
- WP1 → Project management (**MPS**) → *page 3 in "StampaPDF"*
- WP2 → Communication (**CORILA**) → *page 3 in "StampaPDF"*
- WP3.1 → Development of innovative green technologies (**MPS**) → *page 4 in "StampaPDF"*
- WP3.2 → Use of innovative green technologies (**NIB**) → *page 5 in "StampaPDF"*

Overview of Tasks:

WP0	ATT1	Preparazione della scheda e della domanda per la consegna / Priprava prijavnice in vloge za oddajo				
		MPS				
WP1	ATT2	Comitato di coordinamento / Projektni svet				
		MPS	NIB	ESOTECH	CORILA	COMET
	ATT3	Gestione e rendicontazione delle spese / Upravljanje in obračunavanje izdatkov				
		MPS	NIB	ESOTECH	CORILA	COMET
ATT4	Valutazione dell'andamento progettuale / Evalvacija projekta					
	MPS	NIB	ESOTECH	CORILA	COMET	
WP3.1	ATT5	Supporto legale per lo sviluppo di tecnologie verdi innovative / Pravna podpora k razvoju inovativnih zelenih tehnologij				
		MPS	NIB	ESOTECH	CORILA	COMET
	ATT6	Sviluppo di una piattaforma robotica multisensoriale subacquea / Razvoj podvodne multisenzorske robotske platforme				
		MPS				COMET
	ATT7	Sviluppo di un impianto di depurazione modulare / Razvoj modularne čistilne naprave				
			ESOTECH			
ATT8	Monitoraggio ambientale e analisi biochimiche dei campioni di pulizia dell'incrostazione biologica delle navi / Okoljski monitoring in biološko-kemijske analize vzorcev čiščenja ladijske biološke obrasti					
		NIB				
WP3.2	ATT9	Base legale per l'utilizzo di tecnologie verdi innovative / Pravna podlaga za uporabo inovativnih zelenih tehnologij				
		MPS	NIB	ESOTECH	CORILA	COMET
	ATT10	Test dell'applicazione delle tecnologie verdi innovative / Testna uporaba inovativnih zelenih tehnologij				
		MPS	NIB	ESOTECH		COMET
ATT11	Sviluppo di un modello del sistema per la gestione di rifiuti marini pericolosi derivanti dalla pulizia subacquea dell'ISBN / Razvoj modela sistema za upravljanje z nevarnimi morskimi odpadki nastalimi pri podvodnem čiščenju BOTL					
			ESOTECH	CORILA	COMET	
ATT12	Uso pilota delle tecnologie verdi innovative / Pilotna uporaba inovativnih zelenih tehnologij					
	MPS	NIB	ESOTECH	CORILA	COMET	

Overview of Communication Tasks:

WP2	Com 1	Eventi / Dogodki				
		MPS	NIB	ESOTECH	CORILA	COMET
	Com 2	Campagna pubblicitaria / Oglaševalska kampanja				
					CORILA	
	Com 3	Brochure e depliant / Brošure in letaki				
					CORILA	COMET
	Com 5	Sito web / Spletna stran				
		MPS			CORILA	
	Com 6	Account social media / Socialna omrežja				
				CORILA		
Com 7	Newsletter o direct mailing / Newsletter ali direktni mailing					
				CORILA	COMET	
Com 8	Conferenze stampa / Novinarske konference					
		NIB		CORILA		
Com 9	Altre relazioni con i media / Altri rapporti con la stampa					
	MPS	NIB	ESOTECH	CORILA		



UNIONE
EUROPEA
EVROPSKA
UNIJA

Interreg
ITALIA-SLOVENIJA



GreenHull

Timetable:

Date	01.03.2020	01.04.2020	01.05.2020	01.06.2020	01.07.2020	01.08.2020	01.09.2020	01.10.2020	01.11.2020	01.12.2020	01.01.2021	01.02.2021	01.03.2021	01.04.2021	01.05.2021	01.06.2021	01.07.2021	01.08.2021	01.09.2021	01.10.2021	01.11.2021	01.12.2021	01.01.2022	01.02.2022	
Month	1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19	20	21	22	23	24	
ATT1																									
ATT2																									
ATT3																									
ATT4																									
ATT5																									
ATT6																									
ATT7																									
ATT8																									
ATT9																									
ATT10																									
ATT11																									
ATT12																									
Com 1																									
Com 2																									
Com 3																									
Com 5																									
Com 6																									
Com 7																									
Com 8																									
Com 9																									





ATT1	Preparazione della scheda e della domanda per la consegna / Priprava prijavnice in vloge za oddajo			
	MPS			



Done

ATT2	Comitato di coordinamento / Projektni svet																							
	MPS				NIB				ESOTECH				CORILA				COMET							
Date	01.03.2020	01.04.2020	01.05.2020	01.06.2020	01.07.2020	01.08.2020	01.09.2020	01.10.2020	01.11.2020	01.12.2020	01.01.2021	01.02.2021	01.03.2021	01.04.2021	01.05.2021	01.06.2021	01.07.2021	01.08.2021	01.09.2021	01.10.2021	01.11.2021	01.12.2021	01.01.2022	01.02.2022
Month	1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19	20	21	22	23	24

WP1

ATT2 includes:

- formation of the Project Board → 1 representative from each PP
- define dates of the Project Board members meetings → each 6 months or upon request
- define roles of the Project Board members → members responsible for each PP (tasks, reports, deliverables, etc.)

Tasks of the Project Board:

- they report on project progress, financial status, and next 6-month periods planning for each PP
- they solve problems among PPs
- they guarantee for the PP performance and execution
- each PP should buy administrative equipment (computer/printer) as defined in their tasks and budget

Deliverables:

- list of rules for Project Board members (**translated in IT and SLO**)
- record of the meeting (**in IT and SLO**)

ATT3	Gestione e rendicontazione delle spese / Upravljanje in obračunavanje izdatkov																							
	MPS				NIB				ESOTECH				CORILA				COMET							
Date	01.03.2020	01.04.2020	01.05.2020	01.06.2020	01.07.2020	01.08.2020	01.09.2020	01.10.2020	01.11.2020	01.12.2020	01.01.2021	01.02.2021	01.03.2021	01.04.2021	01.05.2021	01.06.2021	01.07.2021	01.08.2021	01.09.2021	01.10.2021	01.11.2021	01.12.2021	01.01.2022	01.02.2022
Month	1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19	20	21	22	23	24

WP1

ATT3 includes:

- Project & Financial manager are leading the activities
- in close cooperation with the responsible person at each PP (Project Board member)

Tasks:

- Financial reports for each PP every 6 months according to the financial plan

Deliverables:

- Financial reports for each PP every 6 months



ATT4	Valutazione dell'andamento progettuale / Evalvacija projekta																							
	MPS				NIB				ESOTECH				CORILA				COMET							
Date	01.03.2020	01.04.2020	01.05.2020	01.06.2020	01.07.2020	01.08.2020	01.09.2020	01.10.2020	01.11.2020	01.12.2020	01.01.2021	01.02.2021	01.03.2021	01.04.2021	01.05.2021	01.06.2021	01.07.2021	01.08.2021	01.09.2021	01.10.2021	01.11.2021	01.12.2021	01.01.2022	01.02.2022
Month	1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19	20	21	22	23	24

WP1

ATT4 includes:

- Project Board defines the evaluation plan

Tasks:

- Evaluation questionnaire for the assessment of the PP tasks each 6 months

Deliverables:

- evaluation report every 6 months (by LP)



ATT5	Supporto legale per lo sviluppo di tecnologie verdi innovative / Pravna podpora k razvoju inovativnih zelenih tehnologij																							
	MPS				NIB				ESOTECH				CORILA				COMET							
Date	01.03.2020	01.04.2020	01.05.2020	01.06.2020	01.07.2020	01.08.2020	01.09.2020	01.10.2020	01.11.2020	01.12.2020	01.01.2021	01.02.2021	01.03.2021	01.04.2021	01.05.2021	01.06.2021	01.07.2021	01.08.2021	01.09.2021	01.10.2021	01.11.2021	01.12.2021	01.01.2022	01.02.2022
Month	1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19	20	21	22	23	24

WP3.1

ATT5 includes:

- Literature review and relevant legislation to support innovative green technologies development

Tasks:

- Literature review about relevant technologies, approaches (**top priority, should be done ASAP**)
- Legal requirements for the technology (**top priority, should be done ASAP**)

Deliverables:

- Report with guidelines and requirements (legal and technical) for the development of the innovative green technologies (in IT and SLO)



ATT6	Sviluppo di una piattaforma robotica multisensoriale subacquea / Razvoj podvodne multisenzorske robotske platforme																							
	MPS																		COMET					
Date	01.03.2020	01.04.2020	01.05.2020	01.06.2020	01.07.2020	01.08.2020	01.09.2020	01.10.2020	01.11.2020	01.12.2020	01.01.2021	01.02.2021	01.03.2021	01.04.2021	01.05.2021	01.06.2021	01.07.2021	01.08.2021	01.09.2021	01.10.2021	01.11.2021	01.12.2021	01.01.2022	01.02.2022
Month	1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19	20	21	22	23	24

WP3.1

ATT6 includes:

- Development of 1. IGT

Tasks:

- Development of the cleaning attachment for the ROV
- Development of the ROV

Deliverables:

- Cleaning attachment for the multisensory ROV
- ROV
- Report of the development with documentation (schematics, etc.)

ATT7	Sviluppo di un impianto di depurazione modulare / Razvoj modularne čistilne naprave																							
			ESOTECH																					
Date	01.03.2020	01.04.2020	01.05.2020	01.06.2020	01.07.2020	01.08.2020	01.09.2020	01.10.2020	01.11.2020	01.12.2020	01.01.2021	01.02.2021	01.03.2021	01.04.2021	01.05.2021	01.06.2021	01.07.2021	01.08.2021	01.09.2021	01.10.2021	01.11.2021	01.12.2021	01.01.2022	01.02.2022
Month	1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19	20	21	22	23	24

WP3.1

ATT7 includes:

- Development of 2. IGT

Tasks:

- Development of the pilot modular wastewater treatment plant with 3 cleaning stages (mechanical, chemical and UV)
- Definition of I/O parameters

Deliverables:

- Pilot wastewater treatment plant
- Report of the development with documentation (schematics, etc.)



ATT8	Monitoraggio ambientale e analisi biochimiche dei campioni di pulizia dell'incrostazione biologica delle navi / Okoljski monitoring in biološko-kemijske analize vzorcev čiščenja ladijske biološke obrasti																			
		NIB																		

Date	01.03.2020	01.04.2020	01.05.2020	01.06.2020	01.07.2020	01.08.2020	01.09.2020	01.10.2020	01.11.2020	01.12.2020	01.01.2021	01.02.2021	01.03.2021	01.04.2021	01.05.2021	01.06.2021	01.07.2021	01.08.2021	01.09.2021	01.10.2021	01.11.2021	01.12.2021	01.01.2022	01.02.2022
Month	1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19	20	21	22	23	24

WP3.1

ATT8 includes:

- Environmental monitoring

Tasks:

- Automatic and real-time monitoring of environmental parameters (turbidity, PAR, conductivity, etc.) during the hull cleaning procedure
- Biological and chemical analysis of sea/wastewater and dry solids as a product of cleaning process
- UV efficiency testing

Deliverables:

- Report of environmental monitoring and chemical analysis to asses the efficacy of the pilot wastewater cleaning plant
- Monitoring equipment



ATT9	Base legale per l'utilizzo di tecnologie verdi innovative / Pravna podlaga za uporabo inovativnih zelenih tehnologij																							
	MPS				NIB				ESOTECH				CORILA				COMET							
Date	01.03.2020	01.04.2020	01.05.2020	01.06.2020	01.07.2020	01.08.2020	01.09.2020	01.10.2020	01.11.2020	01.12.2020	01.01.2021	01.02.2021	01.03.2021	01.04.2021	01.05.2021	01.06.2021	01.07.2021	01.08.2021	01.09.2021	01.10.2021	01.11.2021	01.12.2021	01.01.2022	01.02.2022
Month	1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19	20	21	22	23	24

WP3.2

ATT9 includes:

- Precise and clear instructions on how to performing underwater cleaning

Tasks:

- Precise and clear instructions for the cleaning process
- Define biological and chemical parameters
- Risk assessment for the environment

Deliverables:

- Report and risk assessment for the environment
- Tool for cleaning decisions

ATT10	Test dell'applicazione delle tecnologie verdi innovative / Testna uporaba inovativnih zelenih tehnologij																							
	MPS				NIB				ESOTECH								COMET							
Date	01.03.2020	01.04.2020	01.05.2020	01.06.2020	01.07.2020	01.08.2020	01.09.2020	01.10.2020	01.11.2020	01.12.2020	01.01.2021	01.02.2021	01.03.2021	01.04.2021	01.05.2021	01.06.2021	01.07.2021	01.08.2021	01.09.2021	01.10.2021	01.11.2021	01.12.2021	01.01.2022	01.02.2022
Month	1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19	20	21	22	23	24

WP3.2

ATT10 includes:

- Testing of 1. and 2. IGT

Tasks:

- Testing of the ROV with cleaning attachment
- Testing of the pilot modular wastewater treatment plant

Deliverables:

- Report and results of testing

ATT11	Sviluppo di un modello del sistema per la gestione di rifiuti marini pericolosi derivanti dalla pulizia subacquea dell'ISBN / Razvoj modela sistema za upravljanje z nevarnimi morskimi odpadki nastalimi pri podvodnem čiščenju BOTL																							
									ESOTECH				CORILA				COMET							
Date	01.03.2020	01.04.2020	01.05.2020	01.06.2020	01.07.2020	01.08.2020	01.09.2020	01.10.2020	01.11.2020	01.12.2020	01.01.2021	01.02.2021	01.03.2021	01.04.2021	01.05.2021	01.06.2021	01.07.2021	01.08.2021	01.09.2021	01.10.2021	01.11.2021	01.12.2021	01.01.2022	01.02.2022
Month	1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19	20	21	22	23	24

WP3.2

ATT11 includes:

- Legislation, transborder cooperation for waste management, waste treatment

Tasks:

- Model development for the waste management (from hull cleaning procedures)

Deliverables:

- Several reports for: companies producing waste, companies collecting waste and shipyards
- Organization of workshops (with reports, materials and photos)
- Report about the model for waste management



ATT12	Uso pilota delle tecnologie verdi innovative / Pilotna uporaba inovativnih zelenih tehnologij																							
	MPS				NIB				ESOTECH				CORILA				COMET							
Date	01.03.2020	01.04.2020	01.05.2020	01.06.2020	01.07.2020	01.08.2020	01.09.2020	01.10.2020	01.11.2020	01.12.2020	01.01.2021	01.02.2021	01.03.2021	01.04.2021	01.05.2021	01.06.2021	01.07.2021	01.08.2021	01.09.2021	01.10.2021	01.11.2021	01.12.2021	01.01.2022	01.02.2022
Month	1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19	20	21	22	23	24

WP3.2

ATT12 includes:

- Pilot use of the IGTs

Tasks:

- ROV and pilot wastewater treatment plant testing
- Organization of workshops

Deliverables:

- Pilot use report





UNIONE
EUROPEA
EVROPSKA
UNIJA

Interreg
ITALIA-SLOVENIJA



GreenHull

Com 1	Eventi / Dogodki																							
	MPS				NIB				ESOTECH				CORILA				COMET							
Date	01.03.2020	01.04.2020	01.05.2020	01.06.2020	01.07.2020	01.08.2020	01.09.2020	01.10.2020	01.11.2020	01.12.2020	01.01.2021	01.02.2021	01.03.2021	01.04.2021	01.05.2021	01.06.2021	01.07.2021	01.08.2021	01.09.2021	01.10.2021	01.11.2021	01.12.2021	01.01.2022	01.02.2022
Month	1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19	20	21	22	23	24

WP2

Tasks:

- Organization of 2 big events (at the beginning and at the end of the project)
- Various project dissemination events
- Workshops

Deliverables:

- Various reports related to COM1





Com 2	Campagna pubblicitaria / Oglaševalska kampanja																							
																	CORILA							
Date	01.03.2020	01.04.2020	01.05.2020	01.06.2020	01.07.2020	01.08.2020	01.09.2020	01.10.2020	01.11.2020	01.12.2020	01.01.2021	01.02.2021	01.03.2021	01.04.2021	01.05.2021	01.06.2021	01.07.2021	01.08.2021	01.09.2021	01.10.2021	01.11.2021	01.12.2021	01.01.2022	01.02.2022
Month	1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19	20	21	22	23	24

WP2

Tasks:

- Multimedia tool – Story telling

Deliverables:

- Multimedia tool



Com 3	Brochure e depliant / Brošure in letaki																							
											CORILA					COMET								
Date	01.03.2020	01.04.2020	01.05.2020	01.06.2020	01.07.2020	01.08.2020	01.09.2020	01.10.2020	01.11.2020	01.12.2020	01.01.2021	01.02.2021	01.03.2021	01.04.2021	01.05.2021	01.06.2021	01.07.2021	01.08.2021	01.09.2021	01.10.2021	01.11.2021	01.12.2021	01.01.2022	01.02.2022
Month	1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19	20	21	22	23	24

WP2

Tasks:

- Brochures

Deliverables:

- Various brochures





UNIONE
EUROPEA
EVROPSKA
UNIJA

Interreg
ITALIA-SLOVENIJA



GreenHull

Com 5	Sito web / Spletna stran																							
	MPS												CORILA											
Date	01.03.2020	01.04.2020	01.05.2020	01.06.2020	01.07.2020	01.08.2020	01.09.2020	01.10.2020	01.11.2020	01.12.2020	01.01.2021	01.02.2021	01.03.2021	01.04.2021	01.05.2021	01.06.2021	01.07.2021	01.08.2021	01.09.2021	01.10.2021	01.11.2021	01.12.2021	01.01.2022	01.02.2022
Month	1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19	20	21	22	23	24

WP2

Tasks:

- Web page

Deliverables:

- Web page





Com 6	Account social media / Socialna omrežja																									
																								CORILA		
Date	01.03.2020	01.04.2020	01.05.2020	01.06.2020	01.07.2020	01.08.2020	01.09.2020	01.10.2020	01.11.2020	01.12.2020	01.01.2021	01.02.2021	01.03.2021	01.04.2021	01.05.2021	01.06.2021	01.07.2021	01.08.2021	01.09.2021	01.10.2021	01.11.2021	01.12.2021	01.01.2022	01.02.2022		
Month	1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19	20	21	22	23	24		

WP2

Tasks:

- Presence on social networks

Deliverables:

- Social network profiles and content related to GreenHull project





UNIONE
EUROPEA
EVROPSKA
UNIJA

Interreg
ITALIA-SLOVENIJA



GreenHull

Com 7	Newsletter o direct mailing / Newsletter ali direktni mailing																							
													CORILA						COMET					
Date	01.03.2020	01.04.2020	01.05.2020	01.06.2020	01.07.2020	01.08.2020	01.09.2020	01.10.2020	01.11.2020	01.12.2020	01.01.2021	01.02.2021	01.03.2021	01.04.2021	01.05.2021	01.06.2021	01.07.2021	01.08.2021	01.09.2021	01.10.2021	01.11.2021	01.12.2021	01.01.2022	01.02.2022
Month	1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19	20	21	22	23	24

WP2

Tasks:

- Newsletter or direct marketing

Deliverables:

- Promotion of the project





UNIONE
EUROPEA
EVROPSKA
UNIJA

Interreg
ITALIA-SLOVENIJA



GreenHull

Com 8	Conferenze stampa / Novinarske konference																							
		NIB						CORILA																
Date	01.03.2020	01.04.2020	01.05.2020	01.06.2020	01.07.2020	01.08.2020	01.09.2020	01.10.2020	01.11.2020	01.12.2020	01.01.2021	01.02.2021	01.03.2021	01.04.2021	01.05.2021	01.06.2021	01.07.2021	01.08.2021	01.09.2021	01.10.2021	01.11.2021	01.12.2021	01.01.2022	01.02.2022
Month	1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19	20	21	22	23	24

WP2

Tasks:

- Press conferences

Deliverables:

- Reports from press conferences





Com 9	Altre relazioni con i media / Altri odnosi z javnostmi																							
	MPS						NIB				ESOTECH				CORILA									
Date	01.03.2020	01.04.2020	01.05.2020	01.06.2020	01.07.2020	01.08.2020	01.09.2020	01.10.2020	01.11.2020	01.12.2020	01.01.2021	01.02.2021	01.03.2021	01.04.2021	01.05.2021	01.06.2021	01.07.2021	01.08.2021	01.09.2021	01.10.2021	01.11.2021	01.12.2021	01.01.2022	01.02.2022
Month	1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19	20	21	22	23	24

WP2

Tasks:

- Public relations

Deliverables:

- Reports from public relations
- Media reports about the project



UNIONE
EUROPEA
EVROPSKA
UNIJA

Interreg
ITALIA-SLOVENIJA



GreenHull

3. Financial planning





Financial planning and reporting

SLO: <https://www.ita-slo.eu/sl/izvajanje-projekta>

IT: <https://www.ita-slo.eu/it/attuazione-progettuale>

Write questions to LP and then we will ask MA if needed.

**Read the rules about equipment purchase!!! (3+ quotations for small purchases or tenders)
Follow also the rules for subcontracting!**

SI: https://www.ita-slo.eu/sites/default/files/Annex%20III_Prirocnik_upravicenost_izdatkov.pdf

IT: https://www.ita-slo.eu/sites/default/files/Annex%20III_Manuale%20spese%20ammissibili.pdf

Financial reporting deadlines every 6 months

CRONOPROGRAMMA SEMESTRALE / ŠESTMESEČNI FINANČNI NAČRT

ACRONIMO AKRONIM	LP/VP PP/PP	DENOMINAZIONE PARTNER NAZIV PARTNERJA	STATO DRŽAVA	NATURA GIURIDICA PRAVNI STATUS	2020		2021		2022		2023		TOTALE SKUPAJ	VERIFICA PREGLED
					Periodi di rendicontazione Obdobja poročanja		Periodi di rendicontazione Obdobja poročanja		Periodi di rendicontazione Obdobja poročanja		Periodi di rendicontazione Obdobja poročanja			
					01/09/2019 - 28/02/2020	01/03/2020- 31/08/2020	01/09/2020 - 28/02/2021	01/03/2021- 31/08/2021	01/09/2021 - 28/02/2022	01/03/2022- 31/08/2022	01/09/2022 - 28/02/2023	01/03/2023- 31/08/2023		
					SCADENZA ROK ZA ODDAJO 31/03/2020	SCADENZA ROK ZA ODDAJO 31/09/2020	SCADENZA ROK ZA ODDAJO 31/03/2021	SCADENZA ROK ZA ODDAJO 31/09/2021	SCADENZA ROK ZA ODDAJO 31/03/2022	SCADENZA ROK ZA ODDAJO 31/09/2022	SCADENZA ROK ZA ODDAJO 31/03/2023	SCADENZA ROK ZA ODDAJO 31/09/2023		
GreenHull	LP	Mednarodna podiplomska šola Jožefa Stefana	SLO	PRIV		103'272.80	49'172.70	29'472.70	17'881.80				199'800.00	0.00
GreenHull	PP2	NIB - Nacinalni inštitut za biologijo	SLO	PUB		89'973.60	32'905.20	20'155.20	15'796.00				158'830.00	0.00
GreenHull	PP3	ESOTECH, družba za razvoj in izvajanje ekoloških in energetskih projektov, d.d.	SLO	PRIV		91'116.80	42'812.94	21'975.10	14'683.40				170'588.24	0.00
GreenHull	PP4	CORILA – Consorzio per il coordinamento delle ricerche inerenti al sistema lagunare di Venezia	ITA	PUB		69'505.60	45'090.40	44'290.40	17'593.60				176'480.00	0.00
GreenHull	PP5	COMETS.C.R.L. Cluster Metalmeccanica Friuli Venezia Giulia	ITA	PRIV		73'522.59	48'230.50	36'730.50	17'987.00				176'470.59	0.00
						389'023.90	218'211.74	152'623.90	83'941.80	0.00	0.00	0.00	882'168.83	0.00

We need to spend all allocated money within the 6 month period!

Various

- Media event organization in Venezia
 - unknown development due to the current situation?!?
- Next project meetings
 - in 6 months or when needed
